

Red Line Transformation

Construction Project Updates



Week in Review and Lookahead


Friday, September 15, 2023

The MBTA is holding three more public meetings for the [Ashmont Branch/Mattapan Line track upgrades](#) scheduled to take place for 16 days from Saturday, October 14 through Sunday, October 29:

- [Tuesday, September 19: 6 PM - 8 PM](#)
- [Wednesday, September 27: 6 PM - 8 PM](#)
- [Saturday, September 30: 1 PM - 3 PM](#)




Signal Upgrades

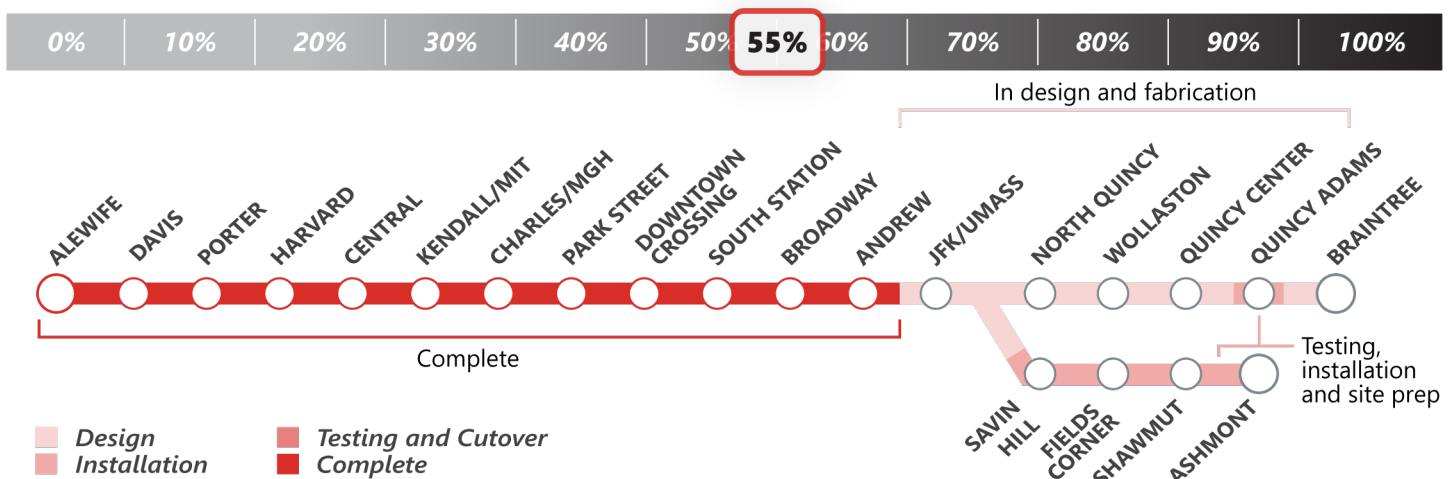

[Signal Upgrades](#): Increase safety and reliability with modernized signals

- ✓ **This Week** | Crews worked in preparation for the upcoming delivery of the signal house at Columbia Junction
- **Lookahead** | Crews are planning signal cable and wire installation and termination at the Ashmont signal house


Codman Yard Expansion and Improvements

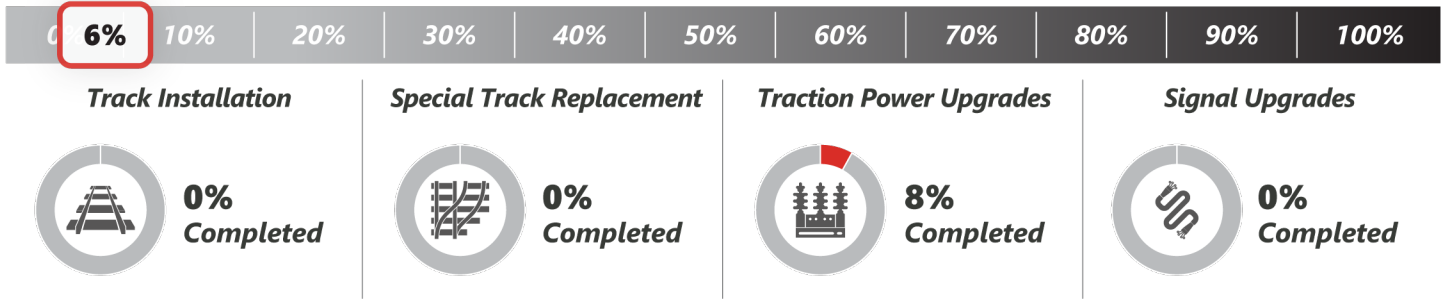

[Codman Yard Expansion and Improvements](#): Upgrade the yard to increase service capacity, replace outdated infrastructure, and enhance safety

- ✓ **This Week** | Crews continued working at zone A by excavating trenches, placing concrete for new duct banks and backfilling, demolishing bedrock, and conducting borings
- **Lookahead** | Crews will continue with duct bank installation and vegetation management

Cabot Yard and Maintenance Facility Updates

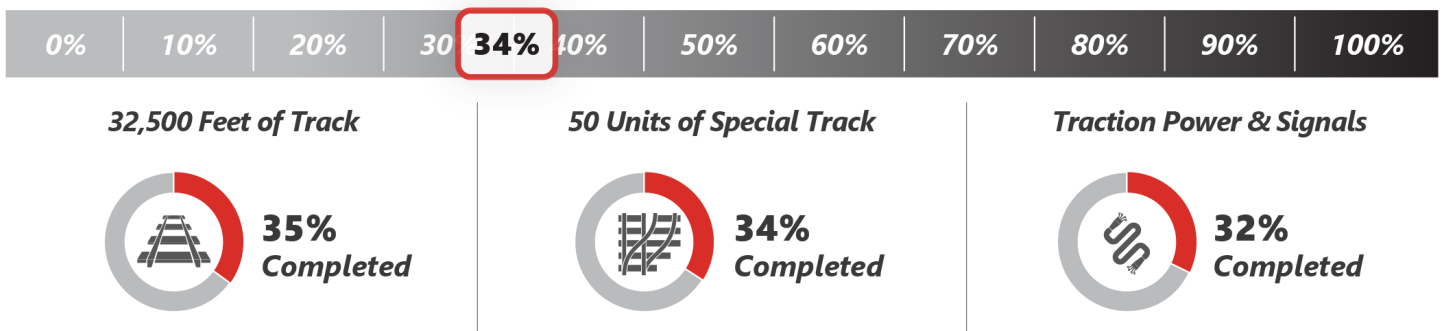

[Cabot Yard](#): Upgrade Cabot Yard to increase service capacity, replace outdated infrastructure, and enhance safety.

- ✓ **This Week** | Crews built sand boxes, and tied and installed rebar in preparation of the duct bank concrete placement next week
- **Lookahead** | Crews will continue to excavate and install duct banks for the next several weeks
